



中国能建沙特凯西姆 II 燃机项目联营体项目部

CEEC EPC JV OF QASSIM 2 PROJECT-KSA

修改码：0

总包项目支付申请单

支付单号：XNZSAF00562-ZF-P-0241

项目名称 中国能建沙特凯西姆 II 燃机项目

项目编号 XNZSAF00562

合同类别	采购	合同编号	ZSAF00549-P-CT-0065-B
合同名称	Qassim 2 中低压动力电缆（在岸）订货合同		
收款单位	单位名称：	Riyadh Cables Group Company	
	账户名称：	Riyadh Cables Group Company	
	开户银行：	BANQUE SAUDI FRANSI	
	银行账号：	SA5655000000044421000135	
合同总额(元)	113,402,485.66	已支付(元)	68,663,726.90
申请支付金额	740,478.32	币种	SAR
项目累计垫支金额	0.00		
是否确认收回	否	预计回收时间	
垫支原因	Batch 3中低压动力电缆锁定铜价后的订单金额为747,194.79SAR（含税），发货款是以实际生产量做最终结算，Batch 3订单第一批货对应货值740,478.32SAR（含税），已具备发货条件，本期将20%预付款与80%发货款一同支付；本期申请支付Batch 3第一批货预付+发货款共计740,478.32*(20%+80%)=740,478.32 SAR，由在岸沙分公司账户支付。（合同约定预付款和发货款为形式发票，发货后24小时内开具税务发票。） 以下是支付条款： 4.2.2 Delivery Against Payment 80% of the Contract Price for each batch of the Equipment under the Purchase Order shall be paid by the Purchaser to the Supplier within 30 days after the completion of production and factory acceptance test of the 发起人(签署)： 邓映金 日期： 2026-05-06		
同意	发起部门岗位经理(签署)：李玲 日期： 2026-05-06		
其他岗位经理(签署)：	宗纪州：同意, 2026-05-07 向魁：同意, 2026-05-07		
预付款支付。已审核资金计划符合支付标准。并收到报审表及形式发票，金额分别为 740,478.32 SAR 740,478.32 SAR ,同意支付 740,478.32 SAR。			
财务专责(签署)：	曹阳	日期：	2026-05-09
同意			
财务经理(签署)：	王勋	日期：	2026-05-10

王振杰:同意, 2026-05-12

项目经理(签署): 彭其润 日期: 2026-05-14

分公司负责人(签署): _____ 日期: _____

财务人员(签署):	曹阳	日期:	2026-05-09	财务部负责人 (签署)	孙伟涛	日期:	2026-05-15
-----------	----	-----	------------	----------------	-----	-----	------------

总会计师(签署): _____ 日期: _____

董事长(签署): _____ 日期: _____



مجموعة كابلات الرياض
Riyadh Cables Group



فاتورة أولية

PROFORMA INVOICE

10159286

RCG Head Office

مكتب المبيعات

Date التاريخ	Sales Order No. رقم طلب البيع	RCG Vat Number الرقم الضريبي
Apr 26, 2026	40217260	300050432610003

Customer :	China Energy International Group Co		
: عناية السيد	شركة تشاينا إنرجي إنترناشيونال جرو		
Address :	الرياض، العقيق، الأمير محمد بن سعد بن		
Tel / Fax			
Customer PO No. رقم أمر الشراء الخاص بالعميل	ZSAF00549-P-CT-0065-B-003- L	Delivery To : مكان التسليم	China Energy International Group Co الرياض، العقيق، الأمير محمد بن سعد بن RIYADH: KSA 12241 SA
Customer No. رقم العميل	10021916	Delivery No. رقم سند التسليم	REF. BELOW
Customer VAT No رقم ضريبة القيمة المضافة للعميل	311502140100003	Delivery Terms شروط التوصيل	Delivered Duty Paid
Payment Terms شروط الدفع	20% DP 80% Before Delivery		

رقم البند Item No.	رمز البند Item Code	المواصفة Description	الوحدة Unit	الكمية Quantity	السعر Price	إجمالي القيمة Total Amount
000010	10015973	5X6mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	KM	5.622	24,980.000	140,437.560
000020	10015974	5X10mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	KM	3.343	36,120.000	120,749.160
000030	10015975	5X16mm ² RC_CU/XL/SW/HFT_1kV_A05_BK	KM	0.960	55,360.000	53,145.600
000040	10015972	5X4mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	KM	1.811	19,290.000	34,934.190
000050	10034900	5X6mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_BK	KM	5.416	30,830.000	166,975.280
000060	10034901	5X10mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_BK	KM	3.005	42,480.000	127,652.400
		صافي القيمة	Net Amount	SAR 643,894.190		
		قيمة الضريبة المضافة	VAT Amount (15%)	SAR 96,584.130		
		قيمة الفاتورة	Total Amount Inc Vat	SAR 740,478.320		

SEVEN HUNDRED FORTY THOUSAND FOUR HUNDRED SEVENTY-EIGHT Saudi Riyal and THIRTY-TWO Halalas

Prepared By	أعدھا		Received By	المستلم
Checked By	راجعھا		Signature	التوقيع
Approved By	إعتمدھا		Date	التاريخ

SAR/R/F/12 01.09.94

Tel: 966-11-2651415
Fax: 966-11-2651423

Email: rcgc@riyadh-cables.com
WWW: www.riyadh-cables.com

P.O. BOX 26862, RIYADH:
11496 KINGDOM OF SAUDI
ARABIA



مجموعة كابلات الرياض
Riyadh Cables Group



فاتورة أولية

PROFORMA INVOICE

10159286

RCG Head Office

مكتب المبيعات

Date التاريخ	Sales Order No. رقم طلب البيع	RCG Vat Number الرقم الضريبي RCG
Apr 26, 2026	40217260	300050432610003

سبعمئة و أربعون ألف و أربعمئة و ثمانية وسبعون ريال سعودي و اثنان وثلاثون هللة

Delivery No's: 0081005648 , 0081005650

The Buyer may request the signed Delivery Note as proof of material receipt within a period of three (3) months from the invoice issue date. Any requests submitted after this period will not be accepted, and the Supplier shall bear no liability in this regard.

يجوز للمشتري طلب إيصال التسليم الموقع كدليل على استلام المواد خلال فترة (3) ثلاثة أشهر من تاريخ إصدار الفاتورة لن يتم قبول أي طلبات يتم تقديمها بعد هذه الفترة ولن يتحمل المورد أي مسؤولية في هذا الصدد

This is a system generated Invoice and no signature or stamp is mandatorily required.

هذه الفاتورة تم إصدارها من قبل النظام ولا تتطلب أي أختام أو توقيعات

Prepared By
Checked By
Approved By

أعدها
راجعها
إعتمدها



Received By
Signature
Date

المستلم
التوقيع
التاريخ

SA/R/F/12 01.09.94

Tel: 966-11-2651415
Fax: 966-11-2651423

Email: rcgc@riyadh-cables.com
WWW: www.riyadh-cables.com

P.O. BOX 26862, RIYADH:
11496 KINGDOM OF SAUDI
ARABIA

合同编号		合同名称	分包单位		合同额（SAR）		备注		合同形式				
ZSAF00549-P-CT-0065-B		凯西姆 II 项目中低压动力电缆订货合同	RIYADH CABLES GROUP COMPANY		59,307,821.59		每批次订单：20%预付：80%发货款		在岸				
支付情况明细表													
序号	期数	第一期	第二期	第三期	第四期	第五期	第六期	第七期	第八期	第九期	第十期	第十一期	第十二期
	时间段	ZSAF00549-P-CT-0065-B-001 订单20%预付款	ZSAF00549-P-CT-0065-B-001 订单中压电缆 80%发货款	ZSAF00549-P-CT-0065-B-001 订单中压电缆 80%发货款	ZSAF00549-P-CT-0065-B-001 订单中压电缆 80%发货款	ZSAF00549-P-CT-0065-B-001 订单中压电缆 80%发货款	ZSAF00549-P-CT-0065-B-002 订单44.962km 电缆 20%预付款	ZSAF00549-P-CT-0065-B-002 订单44.962km 电缆 80%发货款	ZSAF00549-P-CT-0065-B-002 订单3.085 km 电缆 20% 预付款	ZSAF00549-P-CT-0065-B-002 订单3.085 km 电缆 80%发货款	ZSAF00549-P-CT-0065-B-002 订单8.682 km 电缆 20% 预付款	ZSAF00549-P-CT-0065-B-002 订单8.682 km 电缆 80% 发货款	ZSAF00549-P-CT-0065-B-002 订单 20.157km 电缆100% 发货款
1	预付款	3,816,819.26					2,845,226.82		145,334.15		479905.90	479905.90	
2	本期进度款核定金额		4,361,433.03	1,575,284.38	13,324,111.17	26,206.06		14,226,134.10		726670.76	2399529.50	2399529.50	740478.32
3	应扣款项		863,240.41	310,817.40	2,637,487.28	5,274.18		2,845,226.82		145334.15		479905.90	
4	本期实际支付	3,816,819.26	3,498,192.62	1,264,466.98	10,686,623.90	20,931.88	2,845,226.82	11,380,907.28	145,334.15	581336.61	479905.90	1919623.60	740478.32
5	支付比例（%）	6.44%	5.90%	2.13%	18.02%	0.04%	4.80%	19.19%	0.25%	0.98%	0.81%	3.24%	1.25%
6	累计已付金额	3,816,819.26	7,315,011.88	8,579,478.86	19,266,102.75	19,287,034.64	22,132,261.46	33,513,168.74	33,658,502.89	34239839.5	34719745.4	36639369	37379847.32
7	累计已付（%）	6.44%	12.33%	14.47%	32.48%	32.52%	37.32%	56.51%	56.75%	57.73%	58.54%	61.78%	63.03%
	备注	已支付	已支付	已支付	已支付	已支付	已支付	已支付	已支付	已支付	已支付	已支付	本期支付

ZSAF00549-P-CT-0065-B-002 Batch 3订单，本期申请支付Batch 3订单中 20.157低压电缆（对应货值740478.32 SAR），本次申请支付该货值的100%作为发货款，即为740478.32 SAR，由在岸沙分公司账户支付。

																					订铜后单价	订铜+生产后 最终总价		
No	Description	CRef.	Unit	Qty	Riyadh Cable Offer Number	Riyadh Cables Item Code	Riyadh Cables Description	VF CU-USD \$/km	VF AL-USD \$/km	Based Unit Price (\$AR)	Based Total Price(\$AR)	Drum Number	Batch Number	PO	Metal Booking Date	Original Cu	Original Al	Booking Cu	Booking Al	Final Qty	Unit Price after metal booking (\$AR)-Round to 2	Total Price after metal booking (\$AR)		
1	LV Power Cable	LAN5-006 5X6mm2 0.1/6KV	m	1000	25079297	10015973	5X6mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.253	0.000	21.856	21,855.520	Q2-ZM-001	0012592312	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1020	24.98	25479.60		
2	LV Power Cable	LAN5-006 5X6mm2 0.1/6KV	m	1000	25079297	10015973	5X6mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.253	0.000	21.856	21,855.520	Q2-ZM-002	0012592307	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1016	24.98	25379.68		
3	LV Power Cable	LAN5-006 5X6mm2 0.1/6KV	m	1000	25079297	10015973	5X6mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.253	0.000	21.856	21,855.520	Q2-ZM-003	0012592129	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1009	24.98	25204.82		
4	LV Power Cable	LAN5-006 5X6mm2 0.1/6KV	m	1000	25079297	10015973	5X6mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.253	0.000	21.856	21,855.520	Q2-ZM-004	0012592127	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1009	24.98	25204.82		
5	LV Power Cable	LAN5-006 5X6mm2 0.1/6KV	m	1000	25079297	10015973	5X6mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.253	0.000	21.856	21,855.520	Q2-ZM-005	0012613069	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1019	24.98	25454.62		
6	LV Power Cable	LAN5-006 5X6mm2 0.1/6KV	m	540	25079297	10015973	5X6mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.253	0.000	21.856	11,801.981	Q2-ZM-006	0012613063	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	549	24.98	13714.02		
7	LV Power Cable	LAN5-010 5X10mm2 0.1/6KV	m	1000	25079297	10015974	5X10mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.426	0.000	30.863	30,863.420	Q2-ZM-007	0012698563	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1019	36.12	36806.28		
8	LV Power Cable	LAN5-010 5X10mm2 0.1/6KV	m	1000	25079297	10015974	5X10mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.426	0.000	30.863	30,863.420	Q2-ZM-008	0012698553	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1016	36.12	36697.92		
9	LV Power Cable	LAN5-010 5X10mm2 0.1/6KV	m	1000	25079297	10015974	5X10mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.426	0.000	30.863	30,863.420	Q2-ZM-009	0012710610	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1025	36.12	37023.00		
10	LV Power Cable	LAN5-010 5X10mm2 0.1/6KV	m	280	25079297	10015974	5X10mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.426	0.000	30.863	8,024.489	Q2-ZM-010	0012710599	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	283	36.12	10221.96		
11	LV Power Cable	LAN5-016 5X16mm2 0.1/6KV	m	950	25079297	10015975	5X16mm ² RC_CU/XL/SW/ HFT_1kV_A05_BK	0.681	0.000	46.960	44,611.734	Q2-ZM-011	0012594831	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	960	55.36	53145.60		
12	LV Power Cable	LAN5-004 5X4mm2 0.1/6KV	m	1000	25079297	10015972	5X4mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.169	0.000	17.204	17,204.360	Q2-ZM-012	0012589575	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1030	19.29	19868.70		
13	LV Power Cable	LAN5-004 5X4mm2 0.1/6KV	m	780	25079297	10015972	5X4mm ² RM_CU/XL/SW/ HFT_1kV_A05_BK	0.169	0.000	17.204	13,419.401	Q2-ZM-013	0012579302	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	781	19.29	15065.49		
14	LV Power Cable	LAF5-006 5X6mm2 0.1/6KV	m	1000	25079297	10034900	5X6mm ² RM_CU/MGT/XL/ SW/HFT_1kV_A05_BK	0.253	0.000	27.698	27,698.040	Q2-ZM-014	0012669811	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	980	30.83	30213.40		
15	LV Power Cable	LAF5-006 5X6mm2 0.1/6KV	m	1000	25079297	10034900	5X6mm ² RM_CU/MGT/XL/ SW/HFT_1kV_A05_BK	0.253	0.000	27.698	27,698.040	Q2-ZM-015	0012673371	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1026	30.83	31631.58		
16	LV Power Cable	LAF5-006 5X6mm2 0.1/6KV	m	1000	25079297	10034900	5X6mm ² RM_CU/MGT/XL/ SW/HFT_1kV_A05_BK	0.253	0.000	27.698	27,698.040	Q2-ZM-016	0012673366	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	979	30.83	30182.57		
17	LV Power Cable	LAF5-006 5X6mm2 0.1/6KV	m	1000	25079297	10034900	5X6mm ² RM_CU/MGT/XL/ SW/HFT_1kV_A05_BK	0.253	0.000	27.698	27,698.040	Q2-ZM-017	0012676601	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	999	30.83	30799.17		
18	LV Power Cable	LAF5-006 5X6mm2 0.1/6KV	m	1000	25079297	10034900	5X6mm ² RM_CU/MGT/XL/ SW/HFT_1kV_A05_BK	0.253	0.000	27.698	27,698.040	Q2-ZM-018	0012698219	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1012	30.83	31199.96		
19	LV Power Cable	LAF5-006 5X6mm2 0.1/6KV	m	400	25079297	10034900	5X6mm ² RM_CU/MGT/XL/ SW/HFT_1kV_A05_BK	0.253	0.000	27.698	11,079.216	Q2-ZM-019	0012673356	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	420	30.83	12948.60		
20	LV Power Cable	LAF5-010 5X10mm2 0.1/6KV	m	1000	25079297	10034901	5X10mm ² RM_CU/MGT/XL/ SW/HFT_1kV_A05_BK	0.426	0.000	37.221	37,220.880	Q2-ZM-020	0012779381	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1001	42.48	42522.48		
21	LV Power Cable	LAF5-006 5X6mm2 0.1/6KV	m	1000	25079297	10034901	5X10mm ² RM_CU/MGT/XL/ SW/HFT_1kV_A05_BK	0.426	0.000	37.221	37,220.880	Q2-ZM-021	0012779377	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1002	42.48	42564.96		
22	LV Power Cable	LAF5-010 5X10mm2 0.1/6KV	m	1000	25079297	10034901	5X10mm ² RM_CU/MGT/XL/ SW/HFT_1kV_A05_BK	0.426	0.000	37.221	37,220.880	Q2-ZM-022	0012779378	ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00	1002	42.48	42564.96		
23	LV Power Cable	LAF5-010 5X10mm2 0.1/6KV	m	300	25079297	10034901	5X10mm ² RM_CU/MGT/XL/ SW/HFT_1kV_A05_BK	0.426	0.000	37.221	11,166.264	Q2-ZM-023		ZSAF00549-P-CT- 0065-B-003	2026/2/5	9530.00	2458.00	12822.00	3014.00		42.48	0.00		
Total			m	20,230			PO Total Price excluded KSA VAT					569,328.145									20,157		643,894.19	
KSA VAT 15%											85,399.222													96,584.13
PO Total Price with VAT											654,727.367													
																						本期付款 20%+80%	740,478.32	

合同工作完成情况表

合同名称：中国能建沙特凯西姆II燃机项目中低压动力电缆（在岸）订货合同

合同编号：ZSAF00549-P-CT-0065-B

订单编号：ZSAF00549-P-CT-0065-B-3

供货单位：Riyadh Cables Group Company

金额单位: SAR

序号	名称	规格和型号	单位	订单量单				订单量单-Metal booking 后				累计完成		本期完成				箱单号	发运批次	船次	备注
				初始数量	初始单价 (不含税)	初始单价（含 税）	初始合同价	初始数量	Metal booking 后结算单价（不 含税）	结算单价（含 税）	Metal Booking 后合同价	数量 (或比 例)	合价	最终数量 (或比例)	结算单价 (不含税)	结算单价 (含税)	最终合同总价				
一	设备本体																				
(一)	低压动力电缆																				
1	LV Power Cable	LAN5-006 5X6mm2 0.1/6K	m	1000	232.920	21.856	21.856	1000	24.980	28.727	28.727	1,020	29301.540	1,020	24.980	28.727	29301.540		第一批次		
2	LV Power Cable	LAN5-006 5X6mm2 0.1/6K	m	1000	120.160	21.856	21.856	1000	24.980	28.727	28.727	1,016	29186.632	1,016	24.980	28.727	29186.632		第一批次		
3	LV Power Cable	LAN5-006 5X6mm2 0.1/6K	m	1000	10.620	21.856	21.856	1000	24.980	28.727	28.727	1009	28985.543	1009	24.980	28.727	28985.543		第一批次		
4	LV Power Cable	LAN5-006 5X6mm2 0.1/6K	m	1000	95.970	21.856	21.856	1000	24.980	28.727	28.727	1,009	28985.543	1,009	24.980	28.727	28985.543		第一批次		
5	LV Power Cable	LAN5-006 5X6mm2 0.1/6K	m	1000	95.970	21.856	21.856	1000	24.980	28.727	28.727	1,019	29272.813	1,019	24.980	28.727	29272.813		第一批次		
6	LV Power Cable	LAN5-006 5X6mm2 0.1/6K	m	540	95.970	21.856	11,802	540	24.980	28.727	15,513	549	15771.123	549	24.980	28.727	15771.123		第一批次		
7	LV Power Cable	LAN5-010 5X10mm2 0.1/6K	m	1000	41.820	30.863	30,863	1000	36.120	41.538	41,538	1,019	42327.222	1,019	36.120	41.538	42327.222		第一批次		
8	LV Power Cable	LAN5-010 5X10mm2 0.1/6K	m	1000	271.980	30.863	30,863	1000	36.120	41.538	41,538	1016	42202.608	1016	36.120	41.538	42202.608		第一批次		
9	LV Power Cable	LAN5-010 5X10mm2 0.1/6K	m	1000	271.980	30.863	30,863	1000	36.120	41.538	41,538	1025	42576.450	1025	36.120	41.538	42576.450		第一批次		
10	LV Power Cable	LAN5-010 5X10mm2 0.1/6K	m	260	271.980	30.863	8,024	260	36.120	41.538	10,800	283	11755.254	283	36.120	41.538	11755.254		第一批次		
11	LV Power Cable	LAN5-016 5X16mm2 0.1/6K	m	950	271.980	46.960	44,612	950	55.360	63.664	60,481	960	61117.440	960	55.360	63.664	61117.440		第一批次		
12	LV Power Cable	LAN5-004 5X4mm2 0.1/6K	m	1000	271.980	17.204	17,204	1000	19.290	22.184	22,184	1030	22849.005	1030	19.290	22.184	22849.005		第一批次		
13	LV Power Cable	LAN5-004 5X4mm2 0.1/6K	m	780	271.980	17.204	13,419	780	19.290	22.184	17,303	781	17325.314	781	19.290	22.184	17325.314		第一批次		
14	LV Power Cable	LAF5-006 5X6mm2 0.1/6K	m	1000	271.980	27.698	27,698	1000	30.830	35.455	35,455	980	34745.410	980	30.830	35.455	34745.410		第一批次		
15	LV Power Cable	LAF5-006 5X6mm2 0.1/6K	m	1000	271.980	27.698	27,698	1000	30.830	35.455	35,455	1026	36376.317	1026	30.830	35.455	36376.317		第一批次		
16	LV Power Cable	LAF5-006 5X6mm2 0.1/6K	m	1000	271.980	27.698	27,698	1000	30.830	35.455	35,455	979	34709.956	979	30.830	35.455	34709.956		第一批次		
17	LV Power Cable	LAF5-006 5X6mm2 0.1/6K	m	1000	271.980	27.698	27,698	1000	30.830	35.455	35,455	999	35419.046	999	30.830	35.455	35419.046		第一批次		
18	LV Power Cable	LAF5-006 5X6mm2 0.1/6K	m	1000	271.980	27.698	27,698	1000	30.830	35.455	35,455	1012	35879.954	1012	30.830	35.455	35879.954		第一批次		
19	LV Power Cable	LAF5-006 5X6mm2 0.1/6K	m	400	271.980	27.698	11,079	400	30.830	35.455	14,182	420	14890.890	420	30.830	35.455	14890.890		第一批次		
20	LV Power Cable	LAF5-010 5X10mm2 0.1/6K	m	1000	271.980	37.221	37,221	1000	42.480	48.852	48,852	1001	48900.852	1001	42.480	48.852	48900.852		第一批次		
21	LV Power Cable	LAF5-006 5X6mm2 0.1/6K	m	1000	271.980	37.221	37,221	1000	42.480	48.852	48,852	1002	48949.704	1002	42.480	48.852	48949.704		第一批次		
22	LV Power Cable	LAF5-010 5X10mm2 0.1/6K	m	1000	271.980	37.221	37,221	1000	42.480	48.852	48,852	1002	48949.704	1002	42.480	48.852	48949.704		第一批次		
23	LV Power Cable	LAF5-010 5X10mm2 0.1/6K	m	300	271.980	37.221	11,166	300	42.480	48.852	14,656		0.000		42.480	48.852	0.000		第一批次		
三	质保期备品备件																				
1	无																				
四	专用工具																				
1	无																				
六	运费费	已包含					0.00				0.00	-	-	-	-	-	0.00				
五	技术服务费	无					0.00				0.00	-	-	-	-	-	0.00				
	合计						569,328.14				747,194.79		740,478.32	20,157.00			740,478.32				

初始订单总额		569,328.14
Metal Booking 后订单总额		747,194.79
生产完成后最 终总额		740,478.3185



Industry & Facilities Division
Procurement Services
Inspection Report

Page 1 of 14

SIINSPECTION REPORT N° - WQA 2 -PM-EIR- MV/LV CABLE-003	
☐ Initial ☐ Interim ☒ Final ☐ Resident	
Inspection requested by: CEEC	
BV Job Nr :	

Project : THE QASSIM 2 1980MW CCGT INDEPENDENT POWER PROJECT	IPO Ref (If applicable): PU/BRI -24/077
BV Client: CEEC	P/o nr : ZSAF00549-P-CT-0065-B-002
Manufacturer/Vendor : Riyadh Cable Group Company	P/o nr : RC Order#40199347
Sub-Vendor (If applicable): N/A	Previous Inspection (If applicable): N/A
Inspection Location:	Next Inspection (If applicable): TBD
Inspection performed on : 25.04.2026	Total No. of Inspection Days : 1 Days

MATERIAL / SUBJECT OF INSPECTION	ITEM / TAG Nr	QTY As per P/O	QTY Offered for inspection
☒ Refer to attachment section J instead (Indicate if separate material list is provided in attachment)			
LV Cables as per the attached Packing List	Packing List Attached	-	As per Packing List Provided

A – INSPECTION RESULT		
☒ Satisfactory (Without comments)	☐ Satisfactory with comments (Any of trailing Punch or Non Conformity items is still open)	☐ Not Satisfactory (NCR raised during the inspection)
Inspection Summary: As per the Notification, FAT Witness Inspection on LV Cables on 25.04.2026 for QASSIM 2 Project at Vendor (Riyadh Cables LV Cable Factory) Located 2nd Industrial City, Riyadh, KSA. FAT Witness Test has been performed as per the Approved ITP (WQA2-00-AC_-QPH- RCGC- 00200 REV. 00) and the Test Results are Found Satisfactory.		
Open Non Conformities:	☐ Yes, details in section G	☒ No
Open Punch List Items:	☐ Yes, details in section H	☒ No
Release Note Issued:	☐ Yes, number(s): (Release Note number)	☒ No

BV Inspector : Jaffer Saleem	BV Coordinator :
BV Office : Shanghai	Inspection Report Date : 26.04.2025

Distribution: ☒ CLIENT ☒ BV ☐ OTHER :

Attachments Report:

☒ Yes, details in section J ☐ No

B - REFERENCE DOCUMENTATION:

☒ Refer to attachment section J instead

(Indicate if separate document list is provided in attachment)

Title	Reference n°	Rev.	Approval status	Approved by	Date
INSPECTION AND TEST PLAN	WQA2-00-AC-QPH-RCGC-00200	00	Approved	-	-

C - ATTENDEES

Name	Position	Representing
Mr.Jaffer Saleem	E & I Inspector	Bureau Veritas
Mr.Qassim	QC Engineer	Riyadh Cable

D - MEASURING & TESTING EQUIPMENT USED

☒ Refer to attachment section J instead

(Indicate if separate equipment list is provided in attachment)

Equipment Type	Equipment Identity n°	Last Calibration Date	Expiry Date
HV Testing Equipments	5100001195	14.04.2026	14.04.2027
Micro Ohm Meter	5100000735	20.04.2026	20.05.2026
Digital Calliper	5100002144	02.08.2025	02.08.2026
Digital Micrometer	5100002143	02.08.2025	02.08.2026
Oven	51000001117	05.01.2026	05.01.2027
Weight for Hot Set Test	51000000804	08.02.2026	08.02.2027
Measuring Tape	51000000939	07.03.2026	07.09.2026

E - INSPECTION DETAILS

E – General

As per the Notification, FAT Witness Inspection on LV Cables on 25.04.2026 for QASSIM 2 Project at Vendor (Riyadh Cables LV Cable Factory) Located 2nd Industrial City, Riyadh, KSA.

FAT Witness Test has been performed as per the Approved ITP (WQA2-00-AC_-QPH- RCGC- 00200 REV. 00) and the Test Results are Found Satisfactory.

E1 – Details of Witness (W) & Hold (H) Inspection Points

Out of the proposed 22 nos of Cables Drums, FAT Witness has been performed on 06 nos of cable drums.

FAT Witness has been completed on 6 Nos of Cable Drums out of proposed Cable Drums as per the Packing List and FAT has been completed as per ITP as below

2.. Factory Acceptance Test / Final Inspection

2.1 Electrical Test

2.1.1 Conductor resistance at 20°C

Measurement of Conductor Resistance at 20°C on all Witnessed Drums has been performed and the reading has been recorded. Refer FAT Report.

Result : Satisfactory

2.1.2 High voltage test at 3.5KV for 5 minutes

High voltage test at 3.5KV for 5 minutes has been applied on all Witnessed Drums and No Break Down occurs, Refer FAT Report.

Result : Satisfactory

2.2 Sample Test

- 2.2.1 Number of Conductor Wires
- 2.2.2 Conductor diameter (as applicable)
- 2.2.3 Shape of conductor
- 2.2.4 Thickness of mica tape (as applicable)
- 2.2.5 Thickness of XLPE insulation
- 2.2.6 Color of insulation
- 2.2.7 Hot set test with load
- 2.2.8 Hot set after cooling
- 2.2.9 Thickness of inner sheath
- 2.2.10 Number of armor wires (as applicable)
- 2.2.11 Diameter of armor wire (as applicable)
- 2.2.12 Thickness of outer sheath
- 2.2.13 Overall diameter

All the Above Sample Verification Test has been completed on Witnessed 06 Cable Drums out of proposed Cable Drums. All Recorded reading are on the acceptable Range as mentioned in the ITP. Refer FAT Witness Reports.

Result : Satisfactory

As per the Notification, FAT Witness has been completed on 06 Nos of Cable Drums out of proposed 22 Nos of Cable Drums as per the Packing List and FAT has been completed as per ITP (WQA2-00-AC_-QPH- RCGC- 00200 REV. 00) and the Test Results are Found Satisfactory.

E2 – Details of Monitoring and Surveillance Patrols

☐ Tick if conducted during the visit

NIL

E3 – Details of Certificates Review

☒ Tick if conducted during the visit

Document Review

- 1.1 Raw Material Test Certificate
- 1.2 Internal Routine Test Certificate
- 1.3 In-Process Test Report
- 1.4 Calibration Certificate For Testing Equipment
- 1.5 Inspection Test Plan
- 1.6 Packing List

All the above documents has been provided for review during FAT.

All the above reviewed documents has been attached, Refer to attachment in section J

F – HEALTH, SAFETY & ENVIRONMENT COMMENTS

(Comment on Observations and Actions Taken During the Inspection)

Safety Induction Provided ☒

Cleanliness/Tidiness ☒

Trip Hazards ☒

PPE Worn by All Personnel ☒

Safety Procedures Available ☒

Competency ☒

- Note Any Issues Observed: None

G- NON CONFORMITIES

☐ Refer to attachment section J instead

(Indicate if separate punch list is provided in attachment)

Item	Description	Status	Raised on	Report #	Closed on	Report #	Comments
1	N/A						

H – PUNCH LIST

☐ Refer to attachment section J instead

(Indicate if separate punch list is provided in attachment)

Item	Description	Status	Raised on	Report #	Closed on	Report #	Comments
1	N/A						

I - DIGITAL PICTURES



Proposed Cable Drum for FAT Witness



Proposed Cable Drum for FAT Witness




Drum Identification Details



Drum Identification Details



Conductor Resistance

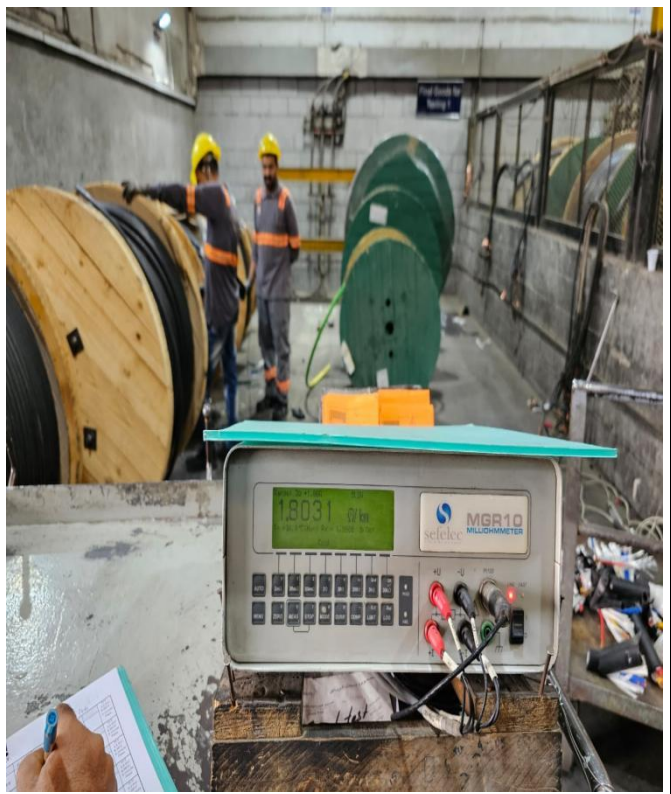

Conductor Resistance



High Voltage Test



High Voltage Test




Over All Diameter



Over All Diameter




Thickness of Outer Sheath

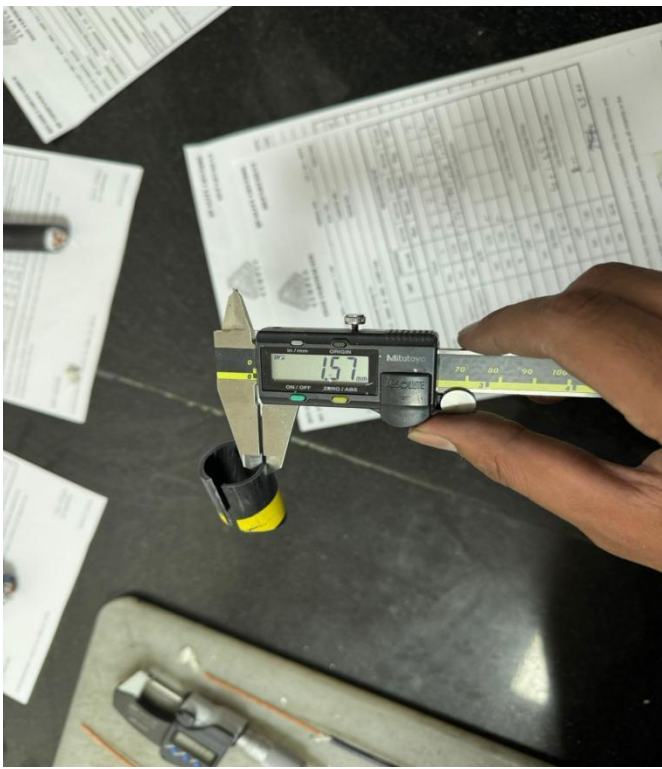

Thickness of Outer Sheath



Thickness of Inner Sheath

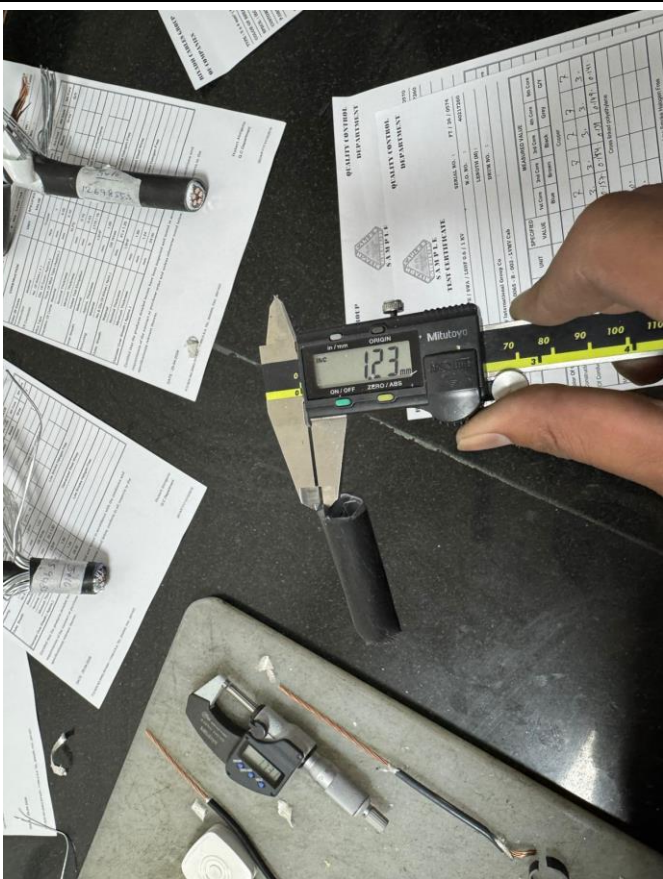

Thickness of Inner Sheath




No of Conductor Wires




No of Conductor Wires




Thickness of XLPE Insulation

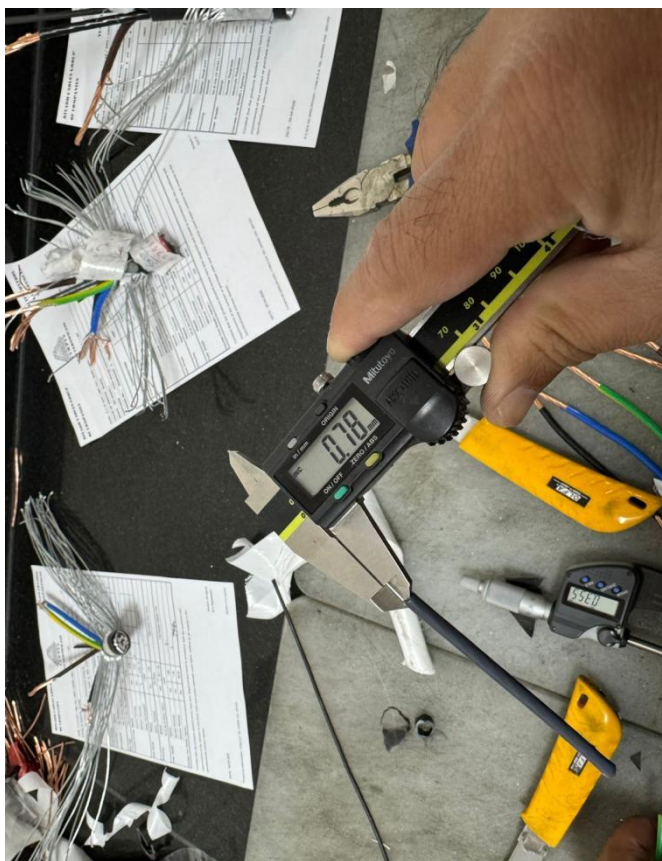


Thickness of XLPE Insulation

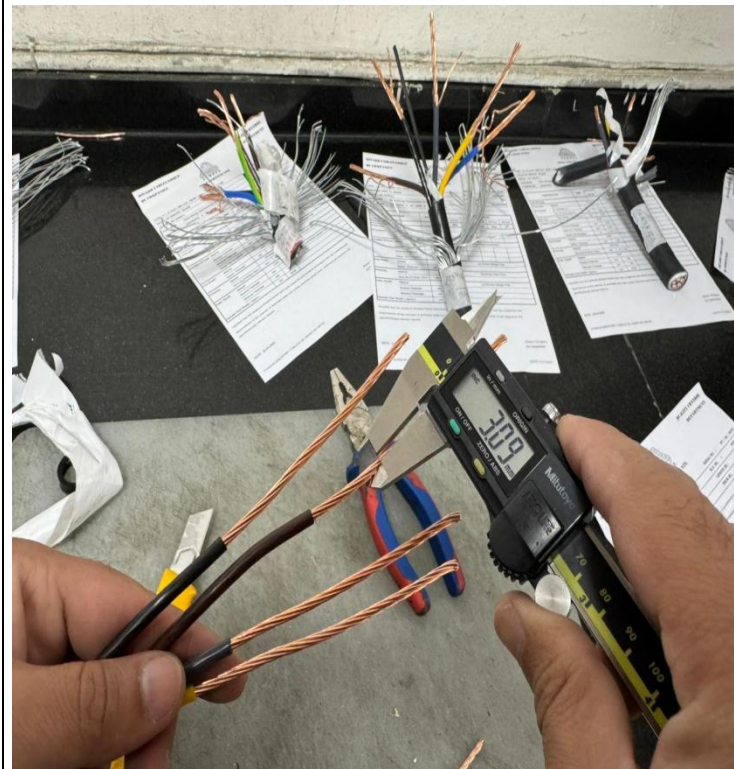

Diameter of the conductor

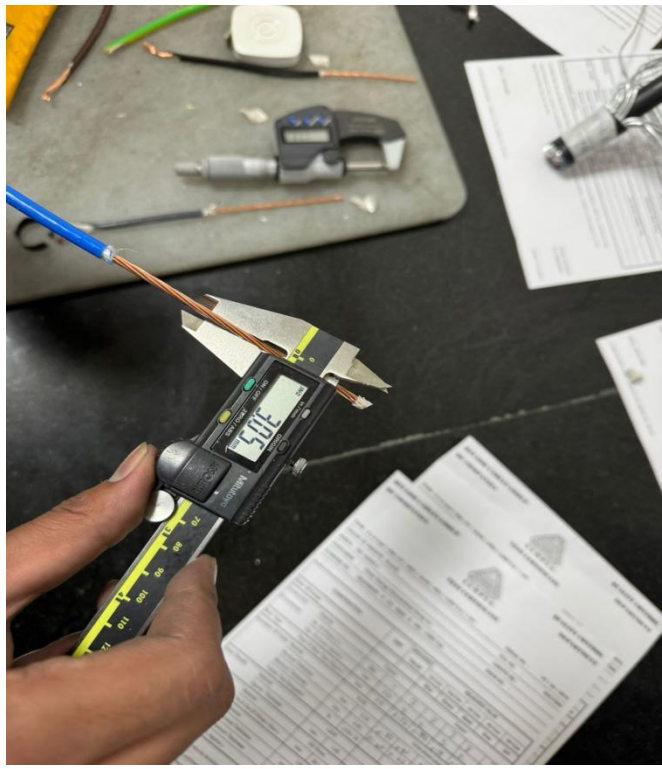


Diameter of the conductor

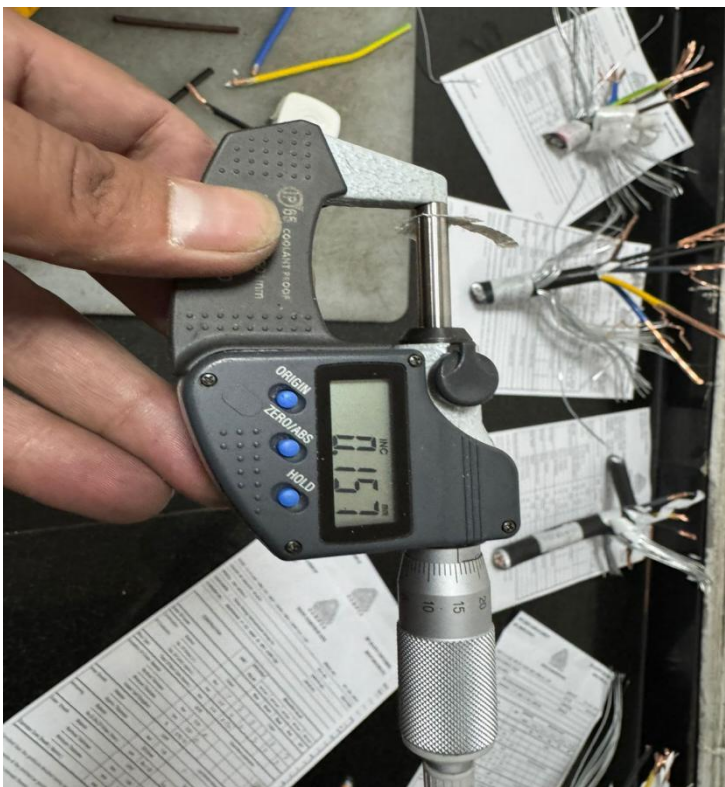


Thickness of mica tape



Thickness of mica tape

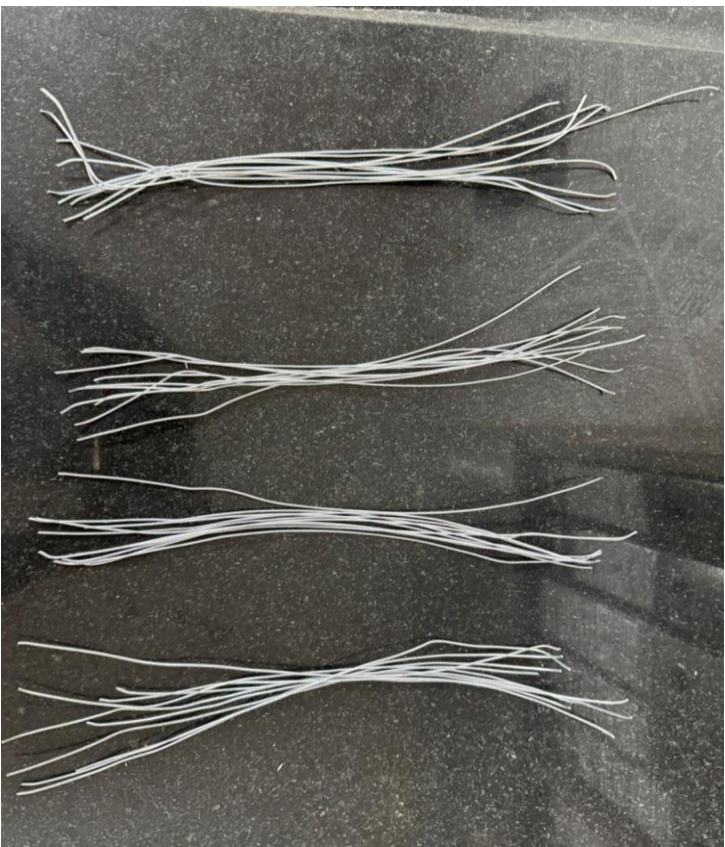

No of Armour Wires

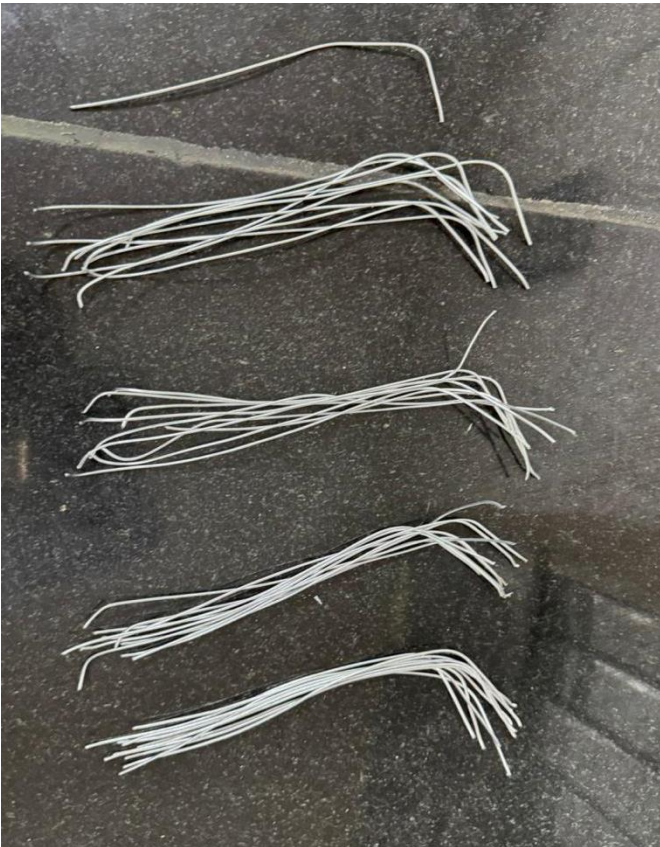

No of Armour Wires



Thickness of Armour Wires



Thickness of Armour Wires



Hot set test with load



Hot set test with load



Hot set test without load



Hot set test without load



Final Measurement for Result



Final Measurement for Result

J – ATTACHMENTS			
Item	Attachment Name	Total Pages	Description
1	FAT Witness Test Report	12	FAT Witness Test Report
2	Routine Test Report	10	Routine Test Report
3	In-Process Test Report	06	In-Process Test Report
4	Packing List	02	Packing List
5	Signed ITP	02	Signed ITP
6	Material Test Certificates(MTC)	5	Material Test Certificates(MTC)
7	Calibration Certificates	16	Calibration Certificates

END OF REPORT



مجموعة كابلات الرياض
Riyadh Cables Group

Delivery Note

81001631

Delivery Date	PO No.	PO Date	Order No.	Order Date	Customer No.
Apr 19, 2026	ZSAF00549-P-CT-0065	Feb 11, 2026	40217260	Feb 11, 2026	10021916
Customer	China Energy International Group Co				
Address	الرياض، العقيق، الأمير محمد بن سعد بن عبدالعزيز RIYADH: KSA				
Plant	REW	Truck No.		Transporter	
Destination :		Customer Loc. :		Contact Person :	

Item	Item Code	Description	S.Loc	DN	Batch	Quantity	Cust. Mat
000010	10015973	5X6mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	001	0012592127	1.009 KM	
000010	10015973	5X6mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	002	0012592129	1.009 KM	
000010	10015973	5X6mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	003	0012592307	1.016 KM	
000010	10015973	5X6mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	004	0012592312	1.020 KM	
000010	10015973	5X6mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	005	0012613069	1.019 KM	
Sub-Total						5.073 KM	
000011	10015973	5X6mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	001	0012613063	0.549 KM	
Sub-Total						0.549 KM	
000020	10015974	5X10mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	001	0012698553	1.016 KM	
000020	10015974	5X10mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	002	0012698563	1.019 KM	
000020	10015974	5X10mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	003	0012710610	1.025 KM	
Sub-Total						3.060 KM	
000021	10015974	5X10mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	001	0012710599	0.283 KM	
Sub-Total						0.283 KM	
000030	10015975	5X16mm ² RC_CU/XL/SW/HFT_1kV_A05_BK	3110	001	0012594831	0.960 KM	
Sub-Total						0.960 KM	
000040	10015972	5X4mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	001	0012589575	1.030 KM	
Sub-Total						1.030 KM	
000041	10015972	5X4mm ² RM_CU/XL/SW/HFT_1kV_A05_BK	3110	001	0012579302	0.781 KM	
Sub-Total						0.781 KM	

Jaffer Saleem

BV Inspector
OBO CEEC
25.04.2026

Prepared By
Receved By



Approved By
Date

SA/R/F/12 01.09.94



Tel: 966-11-2651415
Fax: 966-11-2651423



Email: rcgc@riyadh-cables.com
WWW: www.@riyadh-cables.com



P.O.Box 26862, RIYADH:11496
KINGDOM OF SAUDI ARABIA



Delivery Date	PO No.	PO Date	Order No.	Order Date	Customer No.
Apr 19, 2026	ZSAF00549-P-CT-0065	Feb 11, 2026	40217260	Feb 11, 2026	10021916
Customer	China Energy International Group Co				
Address	الرياض، العقيق، الأمير محمد بن سعد بن عبدالعزيز RIYADH: KSA				
Plant	REW	Truck No.		Transporter	
Destination :		Customer Loc. :		Contact Person :	

Item	Item Code	Description	S.Loc	DN	Batch	Quantity	Cust. Mat
000050	10034900	5X6mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_B K	3110	001	0012698219	1.012 KM	
000050	10034900	5X6mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_B K	3110	002	0012676601	0.999 KM	
000050	10034900	5X6mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_B K	3110	003	0012673371	1.026 KM	
000050	10034900	5X6mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_B K	3110	004	0012673366	0.979 KM	
000050	10034900	5X6mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_B K	3110	005	0012669811	0.980 KM	
Sub-Total						4.996 KM	
000051	10034900	5X6mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_B K	3110	001	0012673356	0.420 KM	
Sub-Total						0.420 KM	
000060	10034901	5X10mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_BK	3104	001	0012779377	1.002 KM	
000060	10034901	5X10mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_BK	3104	002	0012779378	1.002 KM	
000060	10034901	5X10mm ² RM_CU/MGT/XL/SW/HFT_1kV_A05_BK	3104	003	0012779381	1.001 KM	
Sub-Total						3.005 KM	

Jaffer Saleem
BV Inspector
OBO CEEC
25.04.2026



Prepared By	Approved By
Receved By	Date

SA/R/F/12 01.09.94

**QASSIM 2 1980MW CCGT INDEPENDENT POWER PROJECT
SUPPLY CONTRACT FOR LV POWER CABLES, MV POWER
CABLES**

**BETWEEN
CHINA ENERGY INTERNATIONAL GROUP COMPANY LIMITED.**

**AND
RIYADH CABLES GROUP COMPANY**



Contract No.: ZSAF00549-P-CT-0065-B

Date of Signing: August 2025

Place of Signing: Riyadh, Saudi Arabia

起梯



The Purchaser		The Supplier	
Company name (Company stamp)	China Energy International Group Company Limited 	Company name (Company stamp)	 Riyadh Cables Group Company COMMERCIAL DEPT
Signature		Signature	
Address	16th Floor, Hamad Tower (Building No. 7421), King Fahad Branch Road, Al Olaya Dist., Postal Code 12212, Riyadh, Kingdom of Saudi Arabia	Address	P.O. Box 26862, Riyadh: 11496- 2nd Industrial City. Saudi Arabia
Zip code	12212	Zip code	11496
Contact Person:	Zhang Jiantao Zhao Nan	Contact Person:	Mr.Imran Mr.Usman
Tel:	008618028886523 00966507412617	Tel:	+966 55 893 8395 +966 55 948 8545
Email:	zhangjiantao@gedi.com.cn nzhao3318@ceec.net.cn	Email:	m.imran@riyadh-cables.com usman.sharif@riyadh-cables.com
Bank account	QASSIM-2	Bank account	Riyadh Cables Group Company(Saudi Fransi)
Account number	242-310704-003	Account number	SA5655000000044421000135
IBANK Number	SA6345000000242310704003	IBANK Number	SA5655000000044421000135
Taxpayer registration number:	311502140100003	Taxpayer registration number:	300050432610003
Date:	August 30th, 2025	Date:	August 30th 2025



Chapter 4 Terms of Payment

- 4.1 The Supplier shall submit payment documents directly to the Purchaser as stipulated in this Chapter. The Purchaser shall make payments to the Supplier in accordance with the following provisions of this Chapter 4, after receiving the full set of payment documents. Such payments shall be made in SAR.

If the due date for payment is weekend or Chinese Public Holiday or Saudi Arabia Public Holiday, the payment shall be made on the first working day after the weekend or Public Holiday, and such payment shall not be regarded as delay of the payment.

Should the Purchaser considers such documents are not in conformity with the Contract or disputes the amount of any invoices submitted by the Supplier, the Purchaser shall notify the Supplier its reasons within thirty (30) days. The Supplier shall give a prompt response. The payment date shall be recalculated from the date the Purchaser receives qualified payment documents or the Parties reach agreement on the payment amount.

The Purchaser will make payment by telegraphic transfer (T/T).

The payment shall be considered accomplished once the Purchaser's bank has effected the payment to the Supplier's bank account.

- 4.2 The Purchaser shall make payment to the Supplier in the manner set forth as follows:

4.2.1 Advance Payment of Purchase Order

20% of the Contract Price for each Purchase Order shall be paid as advance payment by the Purchaser to the Supplier within 30 days after the Purchaser Order becoming effective and the Purchaser has received all the following documents from the Supplier and found them in order:

- a. a commercial invoice covering the amount of the payment.
- b. the Supplier shall provide manufacturing schedule & delivery schedule, the schedule shall be confirmed by Purchaser.



- c. (i) for the first Purchase Order, an irrevocable Performance Bond in the form as set in Appendix I-3, in favor of the Purchaser for a total amount of 10% of the Tentative Contract Price; and (ii) for any new Purchase Order placed after the aggregate amount of the existing Purchase Orders exceeds the Tentative Contract Price, an irrevocable Performance Bond in the form as set in Appendix I-3, in favor of the Purchaser for a total amount of 10% of the new Purchase Order.

4.2.2 Delivery Against Payment

80% of the Contract Price for each batch of the Equipment under the Purchase Order shall be paid by the Purchaser to the Supplier within 30 days after the completion of production and factory acceptance test of the batch of Equipment and the Purchaser has received and confirmed all the following documents from the Supplier:

- a. a commercial invoice equal to the amount of the payment;
- b. Qualified factory acceptance test report;
- c. Detailed Packing List.

4.2.3 Tax Invoice

The Supplier must provide the Purchaser with a tax invoice for 100% of the value of each batch of Equipment within 24 hours after completion of each loading at the Supplier's workshop.

- 4.2.4 If the Supplier fails to perform the Contract and such behavior has resulted in the losses of the Purchaser, the amount thereof will be deducted from the payment by the Purchaser to offset such losses.

- 4.2.5 The Supplier has the obligation to make out an invoice based on invoice information provided by the Purchaser, otherwise, any loss caused due to the invoice information shall be borne by the Supplier.

- 4.3 Taxes, Customs Duties and Value Added Tax (VAT) incidental to Customs Duties levied by the government on the components, raw materials and semi-manufacturing Goods before delivery according to the agreed delivery

term, shall be borne by the Supplier.

- 4.4 If a Supplemental Agreement is agreed by both Parties which increases or decreases the Contract Price, the payment or deduction will be defined in the Supplemental Agreement.
- 4.5 If in accordance with the stipulations of Chapter 4, 10 and 12, the Supplier is liable to, liquidated damages to the Purchaser for delay delivery, the corresponding amounts shall be paid by the Supplier to the Purchaser within 30 days after receipt of the written notice from the Purchaser stating the amount due. Otherwise, deduction of the corresponding amounts shall be made from any outstanding Contract Price, due and payable, or from the Supplier's Performance Bond.
- 4.6 All banking charges incurred by the Purchaser's Bank shall be borne by the Purchaser. All other banking charges shall be borne by the Supplier.

